

Hand Avenue Collector Road Upgrade Project Update

May 23, 2013

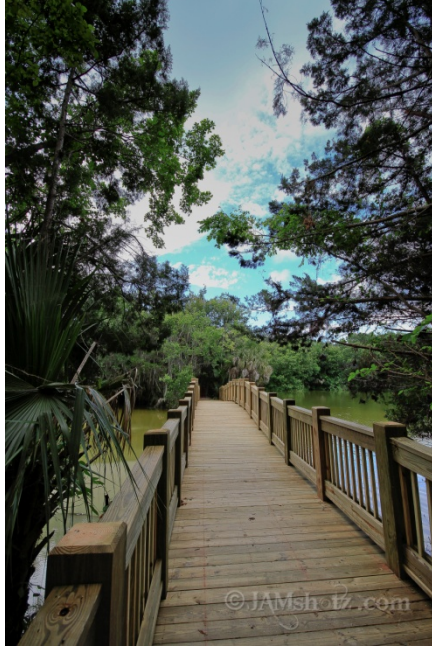


Photo No. 1 – New boardwalk at Central Park

All of the utility work for the project is rapidly moving towards completion. The balance of the 12” water main was completed this week and new water service connections are expected within two weeks. Completion of the storm system in Area 5 at the 500 block of Hand Avenue will have to wait on Health Department approval for the water main.

The large aluminum, elliptical culvert pipe which will provide the canoe/kayak water crossing under the road has been assembled and will be installed the week of May 27th. This will be followed by the excavation of the canals to complete the connection of Central Park Lake 5 on the south side of Hand Avenue and Central Park Lake 4 to the north.

The two sidewalks between Hand and Division which were removed for construction purposes are anticipated to be complete by mid June.

Road demolition and reconstruction has begun in Area 4 (300 and 400 block) of Hand Ave. The first lift of paving is expected to be complete by the middle of July. Roadwork will continue into the 500 block and through the park immediately thereafter.

Residents with questions, comments or concerns are encouraged to contact the City or their Resident Project Representative, Ed Gard, at (407) 539-4515.



Photo No. 2 – Newly dug canal and boardwalk between Central Park Lake North and the adjacent lake to the east



ESG Construction Services, LLC

Some things are not negotiable.

Honesty. Integrity. Trust.

407.539.4515

28 years of Development & Construction Experience

